


Active Water Resource Management (AWRM)

ID	Task Name	Duration	Start	Finish	% Complete	2003		2004		2005	
						1st Half	2nd Half	1st Half	2nd Half	1st Half	
1	Develop Plan for Establishing a Water District & Water Master (Template)	103 days	8/1/2003	12/31/2003	0%						
2	Identify Stream System & Create Water District	80 days	8/1/2003	11/25/2003	0%						
3	Establish Water Master w/ Funding from District	80 days	11/26/2003	3/19/2004	0%						
4	Develop & Adopt Rules & Regulations for Administration	80 days	1/1/2004	4/21/2004	0%						
5	Install Measuring & Metering Devices as Needed	160 days	3/22/2004	10/29/2004	0%						
6	Begin Administering Stream System as Required	1 day	11/1/2004	11/1/2004	0%						
7	Pecos River Basin	489 days	5/1/2003	3/25/2005	17%						
8	Gallinas River	409 days	5/1/2003	12/3/2004	38%						
9	Develop Plan for Establishing a Water District & Water Master (Template)	40 days	5/1/2003	6/26/2003	100%						
10	Identify Stream System & Create Water District	128 days	5/1/2003	10/31/2003	100%						
11	Establish Water Master w/ Funding from District	80 days	1/2/2004	4/22/2004	0%						
12	Develop & Adopt Rules & Regulations for Administration	149 days	6/27/2003	1/30/2004	30%						
13	Install Measuring & Metering Devices as Needed	160 days	4/23/2004	12/2/2004	0%						
14	Begin Administering Stream System as Required	1 day	12/3/2004	12/3/2004	0%						
15	Rio Bonito/Rio Hondo	321 days	1/2/2004	3/25/2005	3%						
16	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%						
17	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%						
18	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%						
19	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%						
20	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%						
21	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%						
22	Rio Penasco	321 days	1/2/2004	3/25/2005	3%						
23	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%						
24	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%						
25	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%						
26	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%						
27	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%						
28	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%						

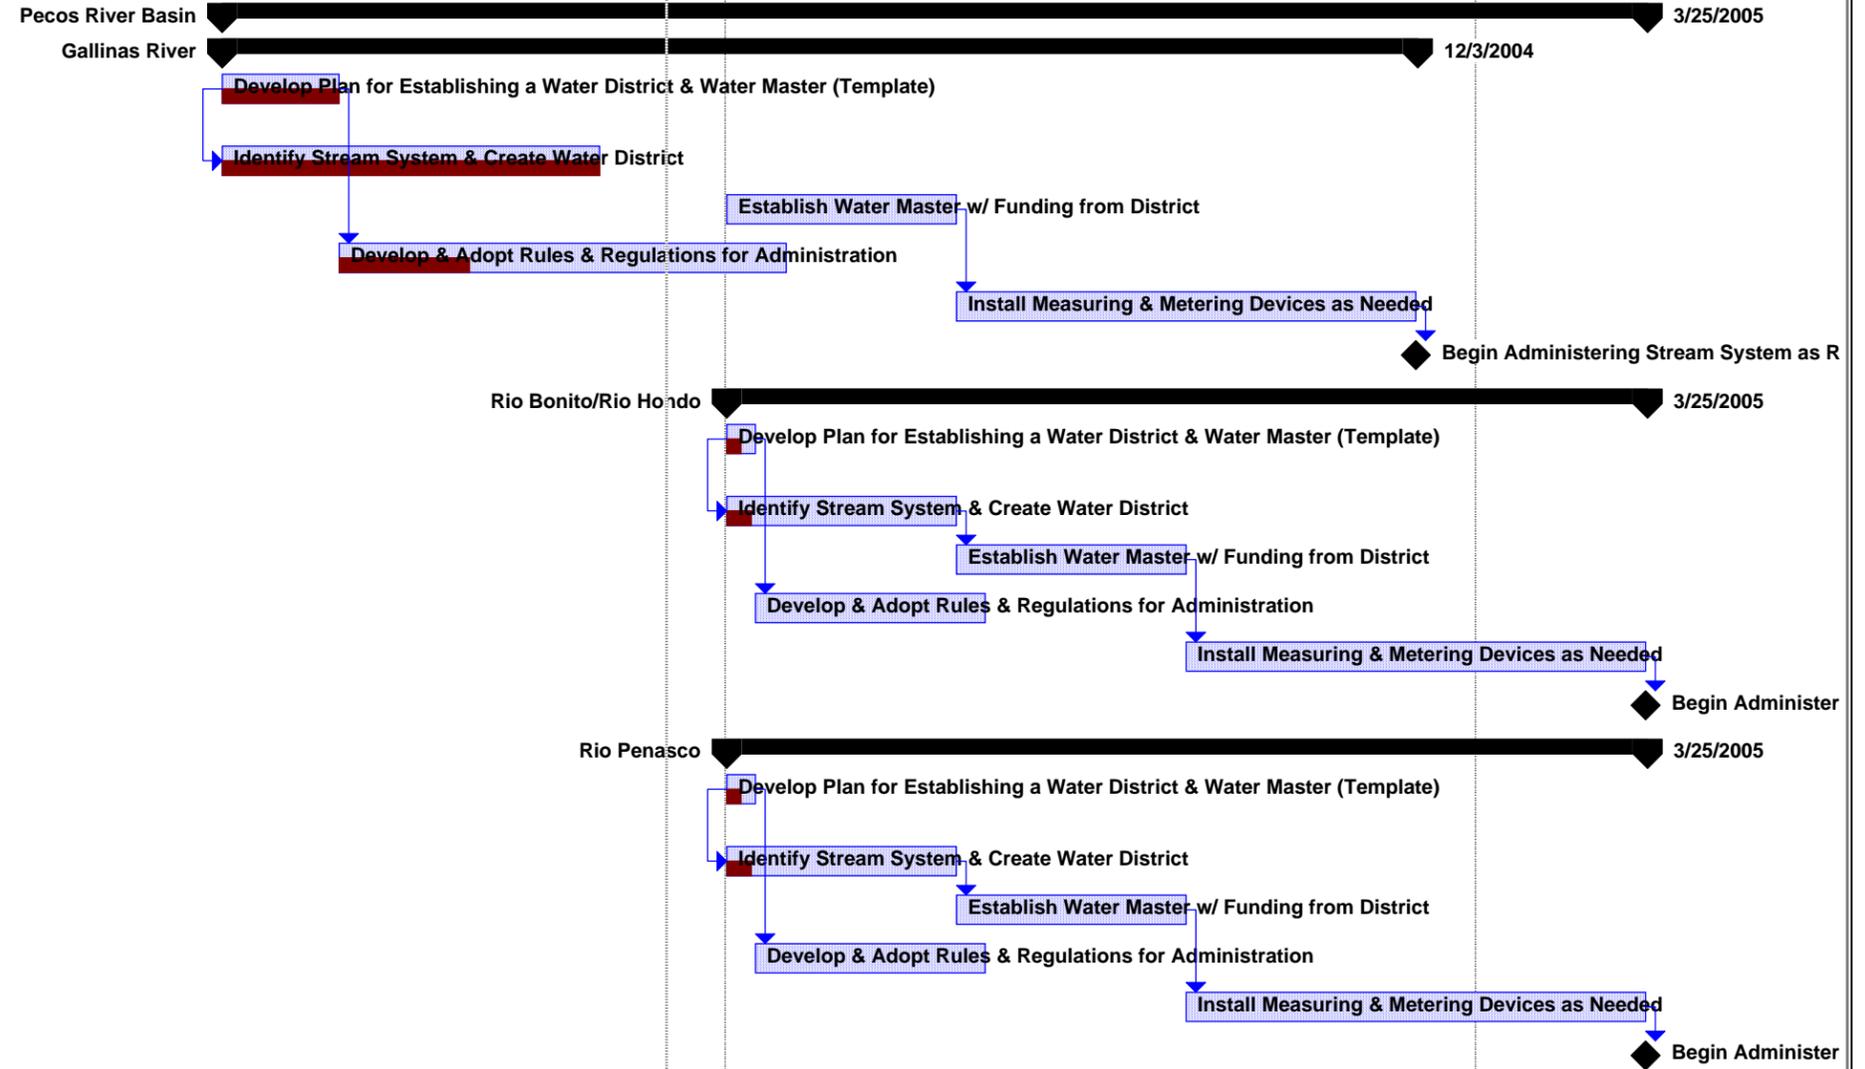

Project: WRPA
Date: 12/3/2003

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

Active Water Resource Management (AWRM)

ID	Task Name	Duration	Start	Finish	% Complete	2003		2004		2005
						1st Half	2nd Half	1st Half	2nd Half	1st Half
29	Upper Rio Grande River Basin	321 days	1/2/2004	3/25/2005	3%		Upper Rio Grande River Basin			3/25/2005
30	Nambe-Pojoaque-Tesuque (N-P-T)	321 days	1/2/2004	3/25/2005	3%		Nambe-Pojoaque-Tesuque (N-P-T)			3/25/2005
31	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%			Develop Plan for Establishing a Water District & Water Master (Template)		
32	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%			Identify Stream System & Create Water District		
33	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%			Establish Water Master w/ Funding from District		
34	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%			Develop & Adopt Rules & Regulations for Administration		
35	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%			Install Measuring & Metering Devices as Needed		
36	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%					◆ Begin Administer
37	Rio Chama	321 days	1/2/2004	3/25/2005	3%		Rio Chama			3/25/2005
38	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%			Develop Plan for Establishing a Water District & Water Master (Template)		
39	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%			Identify Stream System & Create Water District		
40	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%			Establish Water Master w/ Funding from District		
41	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%			Develop & Adopt Rules & Regulations for Administration		
42	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%			Install Measuring & Metering Devices as Needed		
43	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%					◆ Begin Administer
44	San Juan River Basin	251 days	1/2/2004	12/17/2004	38%		San Juan River Basin			12/17/2004
45	Animas & La Plata Rivers	251 days	1/2/2004	12/17/2004	38%		Animas & La Plata Rivers			12/17/2004
46	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%			Develop Plan for Establishing a Water District & Water Master (Template)		
47	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%			Identify Stream System & Create Water District		
48	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%			Establish Water Master w/ Funding from District		
49	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%			Develop & Adopt Rules & Regulations for Administration		
50	Install Measuring & Metering Devices as Needed	160 days	5/7/2004	12/16/2004	90%			Install Measuring & Metering Devices as Needed		
51	Begin Administering Stream System as Required	1 day	12/17/2004	12/17/2004	0%					◆ Begin Administering Stream System a
52	Lower Rio Grande River Basin	321 days	1/2/2004	3/25/2005	3%		Lower Rio Grande River Basin			3/25/2005
53	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%			Develop Plan for Establishing a Water District & Water Master (Template)		
54	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%			Identify Stream System & Create Water District		
55	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%			Establish Water Master w/ Funding from District		
56	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%			Develop & Adopt Rules & Regulations for Administration		
57	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%			Install Measuring & Metering Devices as Needed		
58	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%					◆ Begin Administer

Project: WRPA
Date: 12/3/2003

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

Active Water Resource Management (AWRM)

ID	Task Name	Duration	Start	Finish	% Complete	2003		2004		2005	
						1st Half	2nd Half	1st Half	2nd Half	1st Half	2nd Half
59	Mimbres River Basin	321 days	1/2/2004	3/25/2005	3%						
60	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%						
61	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%						
62	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%						
63	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%						
64	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%						
65	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%						◆ Begin Administer
66	Canadian River Basin	321 days	1/2/2004	3/25/2005	3%						
67	Mora River	321 days	1/2/2004	3/25/2005	3%						
68	Develop Plan for Establishing a Water District & Water Master (Template)	10 days	1/2/2004	1/15/2004	50%						
69	Identify Stream System & Create Water District	80 days	1/2/2004	4/22/2004	10%						
70	Establish Water Master w/ Funding from District	80 days	4/23/2004	8/12/2004	0%						
71	Develop & Adopt Rules & Regulations for Administration	80 days	1/16/2004	5/6/2004	0%						
72	Install Measuring & Metering Devices as Needed	160 days	8/13/2004	3/24/2005	0%						
73	Begin Administering Stream System as Required	1 day	3/25/2005	3/25/2005	0%						◆ Begin Administer

Project: WRPA Date: 12/3/2003	Task Milestone Progress Summary	Rolled Up Task Rolled Up Milestone	Rolled Up Progress Split	External Tasks Project Summary	Group By Summary
----------------------------------	--------------------------------------	---------------------------------------	-----------------------------	-----------------------------------	------------------
