

WATERS (DOMESTIC WELLS)

ID	Task Name	Duration	Start	Finish	% Complete	Qtr 1, 2003	Qtr 2, 2003	Qtr 3, 2003	Qtr 4, 2003	Qtr 1, 2004	Qtr 2, 2004	Qtr 3, 2004	Qtr 4, 2004		
1	Lower Rio Grande Fix DW	115.5 days	Thu 5/1/03	Wed 10/15/03	100%										
2	Sort and Compare	249 hrs	Thu 5/1/03	Mon 6/16/03	100%										
3	Abstract	518 hrs	Mon 6/16/03	Tue 9/16/03	100%										
4	Images to Web	9 hrs	Tue 9/16/03	Wed 9/17/03	100%										
5	QA and Archive	148 hrs	Thu 9/18/03	Wed 10/15/03	100%										
6	Sandia DW	15.38 days	Mon 6/23/03	Tue 7/15/03	100%										
7	Sort and Compare	33 hrs	Mon 6/23/03	Fri 6/27/03	100%										
8	Abstract	69 hrs	Fri 6/27/03	Thu 7/10/03	100%										
9	Images to Web	1 hr	Thu 7/10/03	Thu 7/10/03	100%										
10	QA and Archive	20 hrs	Thu 7/10/03	Tue 7/15/03	100%										
11	Blue Water DW	10.75 days	Tue 7/15/03	Wed 7/30/03	100%										
12	Sort and Compare	23 hrs	Tue 7/15/03	Fri 7/18/03	100%										
13	Abstract	48 hrs	Fri 7/18/03	Mon 7/28/03	100%										
14	Images to Web	1 hr	Mon 7/28/03	Mon 7/28/03	100%										
15	QA and Archive	14 hrs	Mon 7/28/03	Wed 7/30/03	100%										
16	Hot Springs Fix DW	47.25 days	Thu 8/7/03	Wed 10/15/03	100%										
17	Sort and Compare	21 hrs	Thu 8/7/03	Mon 8/11/03	100%										
18	Abstract	43 days	Mon 8/11/03	Fri 10/10/03	100%										
19	Images to Web	1 hr	Fri 10/10/03	Fri 10/10/03	100%										
20	QA and Archive	12 hrs	Fri 10/10/03	Wed 10/15/03	100%										
21	Tularosa Fix DW	42 days	Fri 8/15/03	Wed 10/15/03	100%										
22	Sort and Compare	91 hrs	Fri 8/15/03	Tue 9/2/03	100%										
23	Abstract	188 hrs	Tue 9/2/03	Fri 10/3/03	100%										
24	Images to Web	3 hrs	Fri 10/3/03	Mon 10/6/03	100%										
25	QA and Archive	54 hrs	Mon 10/6/03	Wed 10/15/03	100%										
26	San Juan DW	22.13 days	Fri 8/29/03	Wed 10/1/03	100%										
27	Sort and Compare	48 hrs	Fri 8/29/03	Mon 9/8/03	100%										
28	Abstract	99 hrs	Tue 9/9/03	Thu 9/25/03	100%										
29	Images to Web	2 hrs	Thu 9/25/03	Thu 9/25/03	100%										
30	QA and Archive	28 hrs	Thu 9/25/03	Wed 10/1/03	100%										
31	Upper Pecos DW	31 days	Tue 9/2/03	Wed 10/15/03	100%										
32	Sort and Compare	58 hrs	Tue 9/2/03	Thu 9/11/03	100%										
33	Abstract	120 hrs	Thu 9/11/03	Thu 10/2/03	100%										
34	Images to Web	2 hrs	Thu 10/2/03	Thu 10/2/03	100%										
35	QA and Archive	34 hrs	Wed 10/8/03	Wed 10/15/03	100%										
36	Hondo DW	24.13 days	Wed 9/10/03	Wed 10/15/03	100%										
37	Sort and Compare	52 hrs	Wed 9/10/03	Thu 9/18/03	100%										
38	Abstract	108 hrs	Thu 9/18/03	Tue 10/7/03	100%										
39	Images to Web	2 hrs	Wed 10/8/03	Wed 10/8/03	100%										
40	QA and Archive	31 hrs	Wed 10/8/03	Wed 10/15/03	100%										







Project: WATERS
 Date: Thu 11/13/03






Legend:
 Task: Milestone: Rolled Up Task: Rolled Up Progress:
 Progress: Summary: Rolled Up Milestone: Split: External Tasks:
 Project Summary:

WATERS (DOMESTIC WELLS)

ID	Task Name	Duration	Start	Finish	% Complete	Qtr 1, 2003	Qtr 2, 2003	Qtr 3, 2003	Qtr 4, 2003	Qtr 1, 2004	Qtr 2, 2004	Qtr 3, 2004	Qtr 4, 2004
41	Carlsbad DW	21 days	Tue 9/16/03	Wed 10/15/03	100%				Carlsbad DW 10/15/2003				
42	Sort and Compare	45 hrs	Tue 9/16/03	Tue 9/23/03	100%				Sort and Compare				
43	Abstract	94 hrs	Tue 9/23/03	Thu 10/9/03	100%				Abstract				
44	Images to Web	2 hrs	Thu 10/9/03	Thu 10/9/03	100%				Images to Web				
45	QA and Archive	27 hrs	Thu 10/9/03	Wed 10/15/03	100%				QA and Archive				
46	Fort Sumner DW	8.5 days	Thu 10/2/03	Wed 10/15/03	100%				Fort Sumner DW 10/15/2003				
47	Sort and Compare	18 hrs	Thu 10/2/03	Mon 10/6/03	100%				Sort and Compare				
48	Abstract	38 hrs	Mon 10/6/03	Fri 10/10/03	100%				Abstract				
49	Images to Web	1 hr	Tue 10/14/03	Tue 10/14/03	100%				Images to Web				
50	QA and Archive	11 hrs	Tue 10/14/03	Wed 10/15/03	100%				QA and Archive				
51	Penasco DW	6.25 days	Mon 10/6/03	Wed 10/15/03	100%				Penasco DW 10/15/2003				
52	Sort and Compare	13 hrs	Mon 10/6/03	Tue 10/7/03	100%				Sort and Compare				
53	Abstract	28 hrs	Tue 10/7/03	Tue 10/14/03	100%				Abstract				
54	Images to Web	1 hr	Tue 10/14/03	Tue 10/14/03	100%				Images to Web				
55	QA and Archive	8 hrs	Tue 10/14/03	Wed 10/15/03	100%				QA and Archive				
56	Animas DW	4.38 days	Wed 10/8/03	Wed 10/15/03	100%				Animas DW 10/15/2003				
57	Sort and Compare	9 hrs	Wed 10/8/03	Thu 10/9/03	100%				Sort and Compare				
58	Abstract	19 hrs	Thu 10/9/03	Tue 10/14/03	100%				Abstract				
59	Images to Web	1 hr	Tue 10/14/03	Tue 10/14/03	100%				Images to Web				
60	QA and Archive	6 hrs	Tue 10/14/03	Wed 10/15/03	100%				QA and Archive				
61	Lordsburg DW	4.63 days	Wed 10/8/03	Wed 10/15/03	100%				Lordsburg DW 10/15/2003				
62	Sort and Compare	10 hrs	Wed 10/8/03	Thu 10/9/03	100%				Sort and Compare				
63	Abstract	20 hrs	Thu 10/9/03	Tue 10/14/03	100%				Abstract				
64	Images to Web	1 hr	Tue 10/14/03	Tue 10/14/03	100%				Images to Web				
65	QA and Archive	6 hrs	Tue 10/14/03	Wed 10/15/03	100%				QA and Archive				
66	Hueco DW	3 days	Fri 10/10/03	Wed 10/15/03	100%				Hueco DW 10/15/2003				
67	Sort and Compare	6 hrs	Fri 10/10/03	Fri 10/10/03	100%				Sort and Compare				
68	Abstract	13 hrs	Fri 10/10/03	Wed 10/15/03	100%				Abstract				
69	Images to Web	1 hr	Wed 10/15/03	Wed 10/15/03	100%				Images to Web				
70	QA and Archive	4 hrs	Wed 10/15/03	Wed 10/15/03	100%				QA and Archive				
71	Las Animas Creek Fix DW	2.13 days	Fri 10/10/03	Wed 10/15/03	100%				Las Animas Creek Fix DW 10/15/2003				
72	Sort and Compare	4 hrs	Fri 10/10/03	Fri 10/10/03	100%				Sort and Compare				
73	Abstract	9 hrs	Fri 10/10/03	Tue 10/14/03	100%				Abstract				
74	Images to Web	1 hr	Tue 10/14/03	Tue 10/14/03	100%				Images to Web				
75	QA and Archive	3 hrs	Tue 10/14/03	Wed 10/15/03	100%				QA and Archive				
76	Salt Basin Fix DW	1.88 days	Tue 10/14/03	Wed 10/15/03	100%				Salt Basin Fix DW 10/15/2003				
77	Sort and Compare	4 hrs	Tue 10/14/03	Tue 10/14/03	100%				Sort and Compare				
78	Abstract	8 hrs	Tue 10/14/03	Wed 10/15/03	100%				Abstract				
79	Images to Web	1 hr	Wed 10/15/03	Wed 10/15/03	100%				Images to Web				
80	QA and Archive	2 hrs	Wed 10/15/03	Wed 10/15/03	100%				QA and Archive				


Project: WATERS
Date: Thu 11/13/03

Task  Milestone  Rolled Up Task  Rolled Up Progress  External Tasks  Group By Summary 

Progress  Summary  Rolled Up Milestone  Split  Project Summary 

WATERS (DOMESTIC WELLS)

ID	Task Name	Duration	Start	Finish	% Complete	Qtr 1, 2003	Qtr 2, 2003	Qtr 3, 2003	Qtr 4, 2003	Qtr 1, 2004	Qtr 2, 2004	Qtr 3, 2004	Qtr 4, 2004
81	Viriden Valley DW	1.38 days	Tue 9/2/03	Wed 9/3/03	50%								
82	Sort and Compare	3 hrs	Tue 9/2/03	Tue 9/2/03	100%								
83	Abstract	5 hrs	Tue 9/2/03	Tue 9/2/03	50%								
84	Images to Web	1 hr	Wed 9/3/03	Wed 9/3/03	0%								
85	QA and Archive	2 hrs	Wed 9/3/03	Wed 9/3/03	0%								
86	Gallup DW	9.88 days	Mon 9/15/03	Fri 9/26/03	77%								
87	Sort and Compare	21 hrs	Mon 9/15/03	Wed 9/17/03	100%								
88	Abstract	44 hrs	Wed 9/17/03	Thu 9/25/03	91%								
89	Images to Web	1 hr	Thu 9/25/03	Thu 9/25/03	0%								
90	QA and Archive	13 hrs	Thu 9/25/03	Fri 9/26/03	0%								
91	Estancia DW	53.25 days	Fri 10/17/03	Tue 1/6/04	21%								
92	Sort and Compare	115 hrs	Fri 10/17/03	Thu 11/6/03	78%								
93	Abstract	239 hrs	Thu 11/6/03	Tue 12/23/03	0%								
94	Images to Web	4 hrs	Tue 12/23/03	Tue 12/23/03	0%								
95	QA and Archive	68 hrs	Wed 12/24/03	Tue 1/6/04	0%								
96	Canadian River DW	31.88 days	Tue 1/6/04	Thu 2/19/04	25%								
97	Sort and Compare	69 hrs	Tue 1/6/04	Mon 1/19/04	92%								
98	Abstract	142 hrs	Mon 1/19/04	Wed 2/11/04	0%								
99	Images to Web	3 hrs	Wed 2/11/04	Thu 2/12/04	0%								
100	QA and Archive	41 hrs	Thu 2/12/04	Thu 2/19/04	0%								
101	Capitan DW	6.13 days	Fri 2/20/04	Mon 3/1/04	0%								
102	Sort and Compare	13 hrs	Fri 2/20/04	Mon 2/23/04	0%								
103	Abstract	27 hrs	Mon 2/23/04	Thu 2/26/04	0%								
104	Images to Web	1 hr	Fri 2/27/04	Fri 2/27/04	0%								
105	QA and Archive	8 hrs	Fri 2/27/04	Mon 3/1/04	0%								
106	Curry DW	9.63 days	Tue 3/2/04	Mon 3/15/04	60%								
107	Sort and Compare	21 hrs	Tue 3/2/04	Thu 3/4/04	100%								
108	Abstract	43 hrs	Thu 3/4/04	Thu 3/11/04	59%								
109	Images to Web	1 hr	Fri 3/12/04	Fri 3/12/04	0%								
110	QA and Archive	12 hrs	Fri 3/12/04	Mon 3/15/04	0%								
111	Gila-San Francisco DW	26 days	Tue 3/16/04	Tue 4/20/04	16%								
112	Sort and Compare	59 hrs	Tue 3/16/04	Thu 3/25/04	56%								
113	Abstract	122 hrs	Thu 3/25/04	Thu 4/15/04	0%								
114	Images to Web	2 hrs	Thu 4/15/04	Thu 4/15/04	0%								
115	QA and Archive	25 hrs	Thu 4/15/04	Tue 4/20/04	0%								
116	Lea County DW	84.38 days	Wed 4/21/04	Tue 8/17/04	38%								
117	Sort and Compare	182 hrs	Wed 4/21/04	Fri 5/21/04	100%								
118	Abstract	378 hrs	Fri 5/21/04	Tue 7/27/04	20%								
119	Images to Web	7 hrs	Wed 7/28/04	Wed 7/28/04	0%								
120	QA and Archive	108 hrs	Wed 7/28/04	Tue 8/17/04	0%								

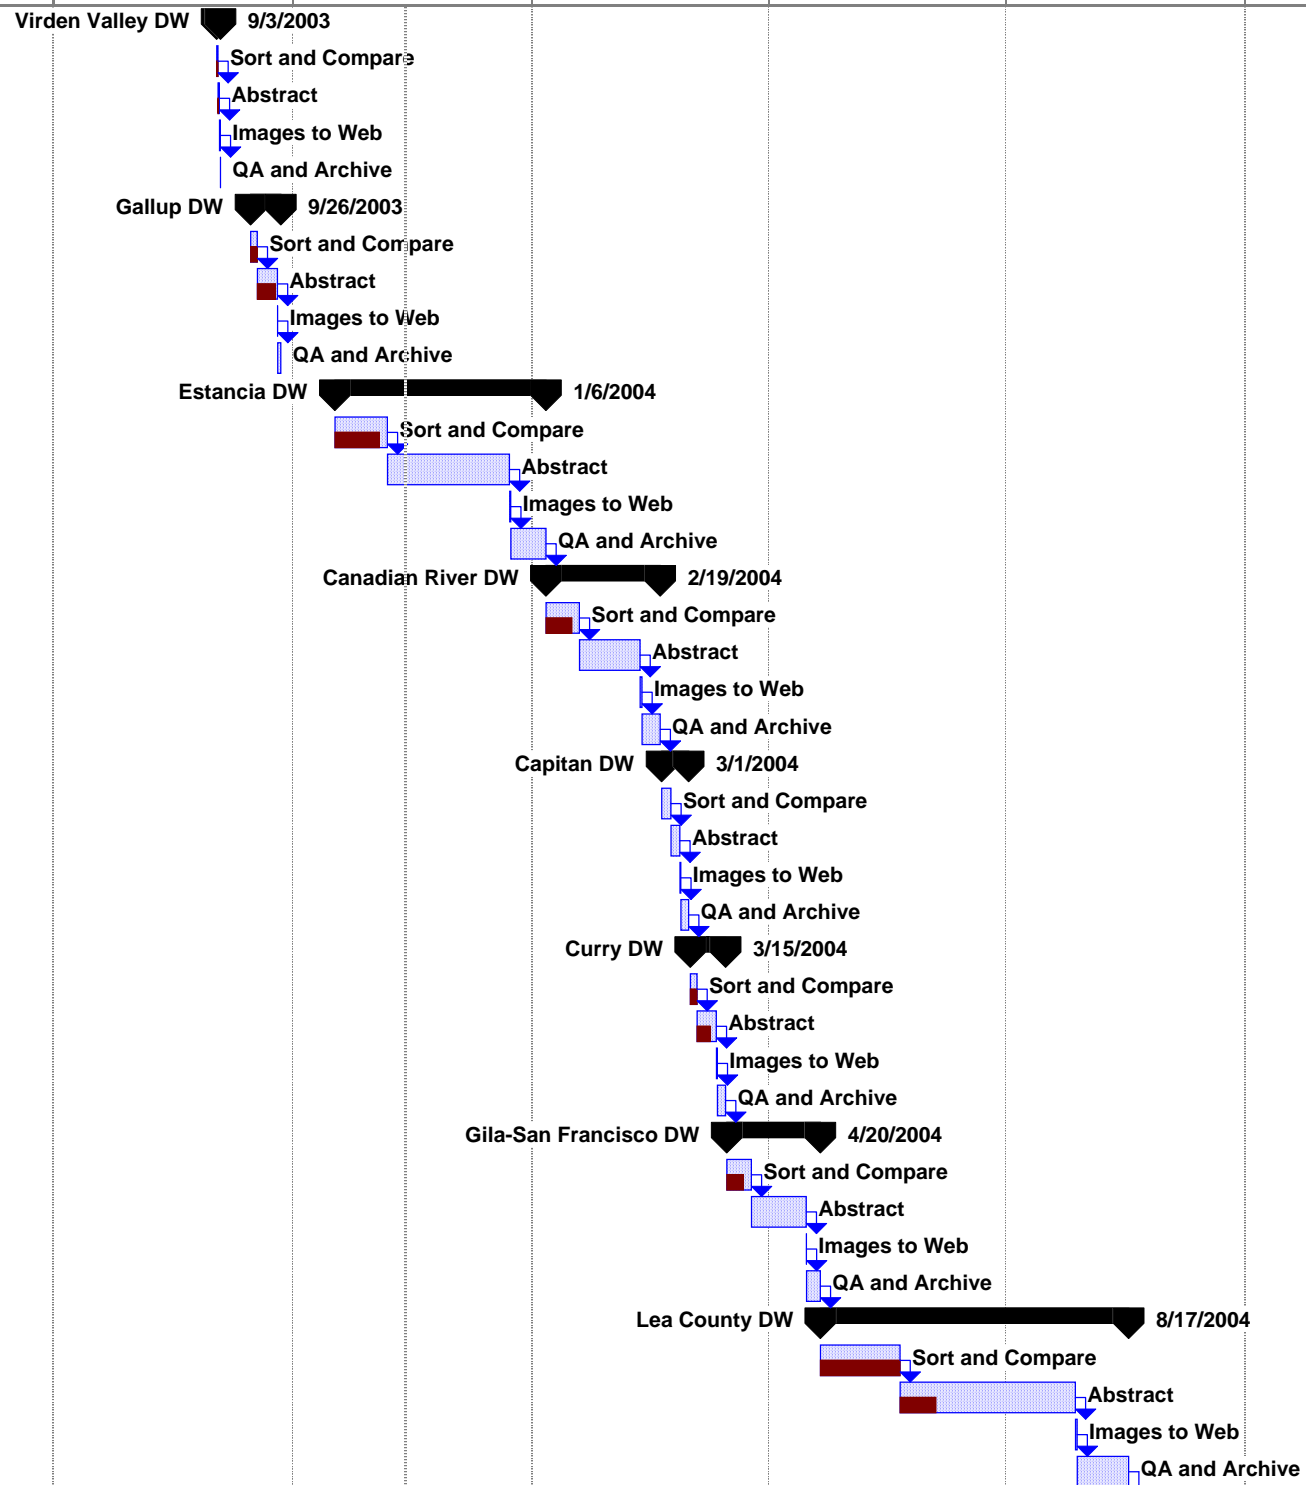


Project: WATERS
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

WATERS (DOMESTIC WELLS)

ID	Task Name	Duration	Start	Finish	% Complete	Qtr 1, 2003	Qtr 2, 2003	Qtr 3, 2003	Qtr 4, 2003	Qtr 1, 2004	Qtr 2, 2004	Qtr 3, 2004	Qtr 4, 2004
121	Middle Rio Grande DW	467.13 days	Tue 8/17/04	Thu 6/1/06	24%								
122	Sort and Compare	1009 hrs	Tue 8/17/04	Wed 2/9/05	89%								
123	Abstract	2093 hrs	Wed 2/9/05	Fri 2/10/06	0%								
124	Images to Web	37 hrs	Fri 2/10/06	Thu 2/16/06	0%								
125	QA and Archive	598 hrs	Thu 2/16/06	Thu 6/1/06	0%								
126	Mimbres DW	72.75 days	Thu 6/1/06	Tue 9/12/06	28%								
127	Sort and Compare	157 hrs	Thu 6/1/06	Thu 6/29/06	100%								
128	Abstract	326 hrs	Thu 6/29/06	Thu 8/24/06	2%								
129	Images to Web	6 hrs	Thu 8/24/06	Fri 8/25/06	0%								
130	QA and Archive	93 hrs	Fri 8/25/06	Tue 9/12/06	0%								
131	Nutt-Hockett DW	2.38 days	Tue 9/12/06	Thu 9/14/06	35%								
132	Sort and Compare	5 hrs	Tue 9/12/06	Tue 9/12/06	100%								
133	Abstract	10 hrs	Tue 9/12/06	Thu 9/14/06	17%								
134	Images to Web	1 hr	Thu 9/14/06	Thu 9/14/06	0%								
135	QA and Archive	3 hrs	Thu 9/14/06	Thu 9/14/06	0%								
136	Playas Valley DW	7.88 days	Thu 9/14/06	Tue 9/26/06	0%								
137	Sort and Compare	17 hrs	Thu 9/14/06	Mon 9/18/06	0%								
138	Abstract	35 hrs	Mon 9/18/06	Mon 9/25/06	0%								
139	Images to Web	1 hr	Mon 9/25/06	Mon 9/25/06	0%								
140	QA and Archive	10 hrs	Mon 9/25/06	Tue 9/26/06	0%								
141	Portales DW	29.88 days	Tue 9/26/06	Tue 11/7/06	16%								
142	Sort and Compare	65 hrs	Tue 9/26/06	Fri 10/6/06	59%								
143	Abstract	134 hrs	Fri 10/6/06	Tue 10/31/06	0%								
144	Images to Web	2 hrs	Tue 10/31/06	Tue 10/31/06	0%								
145	QA and Archive	38 hrs	Tue 10/31/06	Tue 11/7/06	0%								
146	Upper Rio Grande DW	116.75 days	Tue 11/7/06	Thu 4/19/07	24%								
147	Sort and Compare	252 hrs	Tue 11/7/06	Wed 12/20/06	89%								
148	Abstract	523 hrs	Wed 12/20/06	Thu 3/22/07	0%								
149	Images to Web	9 hrs	Thu 3/22/07	Fri 3/23/07	0%								
150	QA and Archive	150 hrs	Fri 3/23/07	Thu 4/19/07	0%								
151	Roswell DW	76.5 days	Thu 4/19/07	Fri 8/3/07	90%								
152	Sort and Compare	165 hrs	Thu 4/19/07	Thu 5/17/07	100%								
153	Abstract	343 hrs	Thu 5/17/07	Tue 7/17/07	100%								
154	Images to Web	6 hrs	Tue 7/17/07	Wed 7/18/07	100%								
155	QA and Archive	98 hrs	Wed 7/18/07	Fri 8/3/07	38%								
156	San Simon DW	1.88 days	Fri 8/3/07	Tue 8/7/07	10%								
157	Sort and Compare	4 hrs	Fri 8/3/07	Mon 8/6/07	38%								
158	Abstract	8 hrs	Mon 8/6/07	Tue 8/7/07	0%								
159	Images to Web	1 hr	Tue 8/7/07	Tue 8/7/07	0%								
160	QA and Archive	2 hrs	Tue 8/7/07	Tue 8/7/07	0%								














Project: WATERS
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			


WATERS (DOMESTIC WELLS)

ID	Task Name	Duration	Start	Finish	% Complete	Qtr 1, 2003	Qtr 2, 2003	Qtr 3, 2003	Qtr 4, 2003	Qtr 1, 2004	Qtr 2, 2004	Qtr 3, 2004	Qtr 4, 2004
161	Tucumcari DW	10.13 days	Tue 8/7/07	Tue 8/21/07	0%								
162	Sort and Compare	22 hrs	Tue 8/7/07	Fri 8/10/07	0%								
163	Abstract	45 hrs	Fri 8/10/07	Fri 8/17/07	0%								
164	Images to Web	1 hr	Fri 8/17/07	Fri 8/17/07	0%								
165	QA and Archive	13 hrs	Mon 8/20/07	Tue 8/21/07	0%								

Project: WATERS
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			

WATERS (DOMESTIC WELLS)

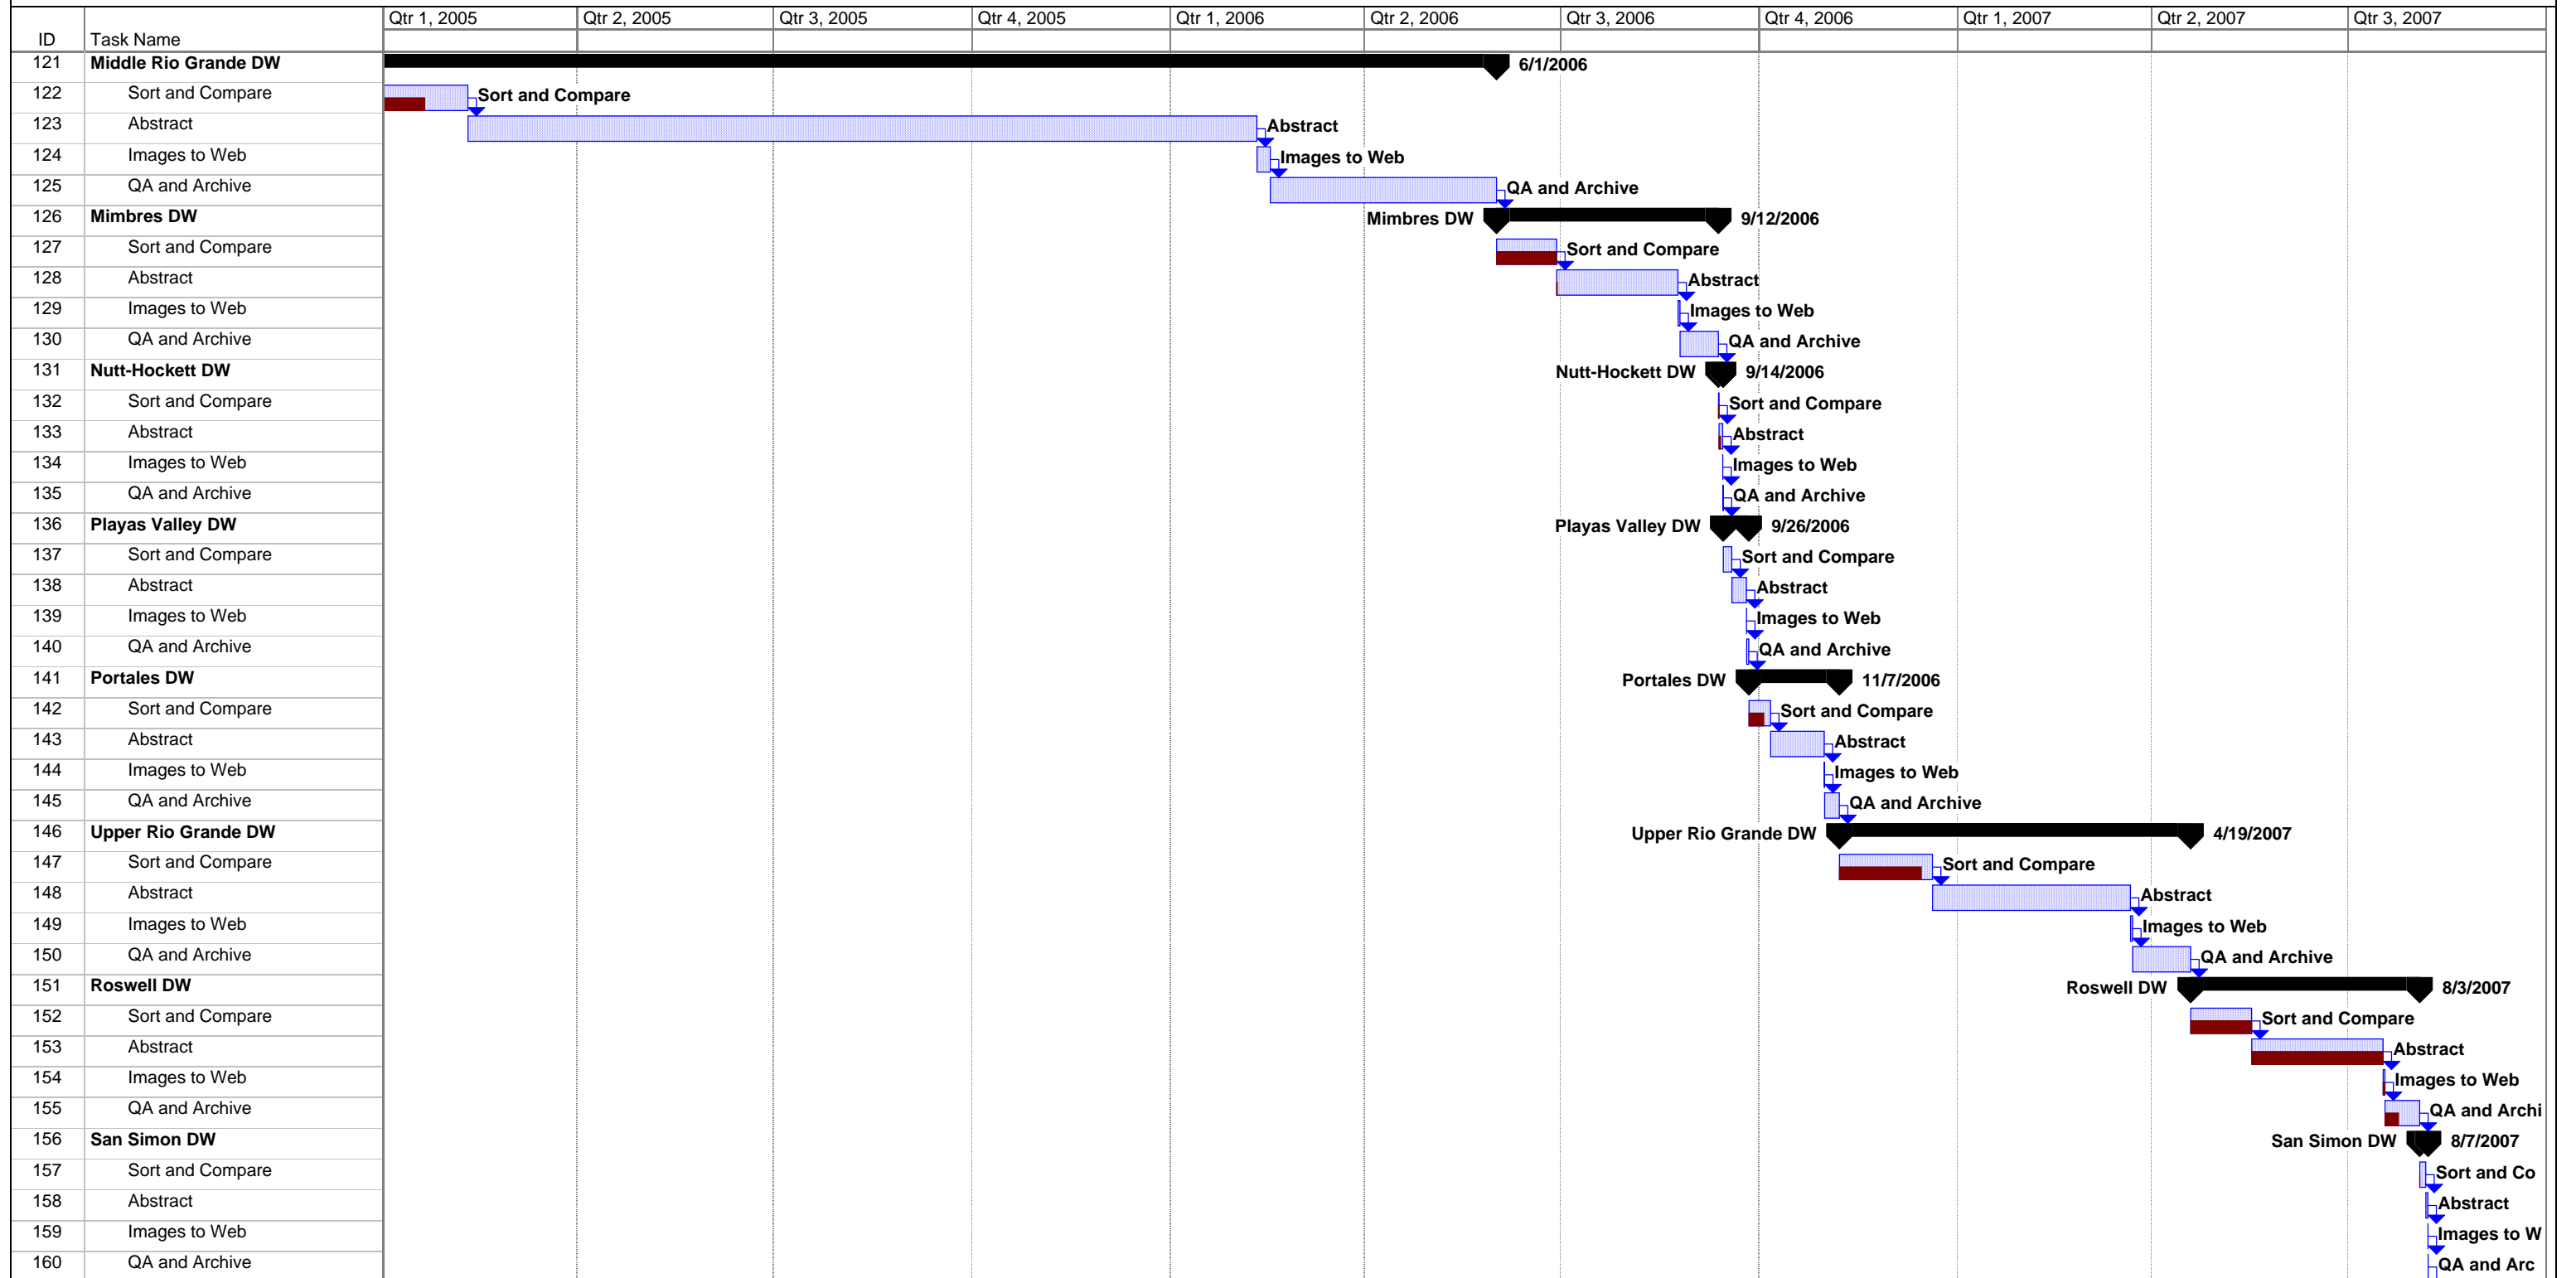


Project: WATERS
 Date: Thu 11/13/03

Legend:
 Task: [Blue box] Milestone: [Diamond] Rolled Up Task: [Blue box] Rolled Up Progress: [Black bar] External Tasks: [Grey bar] Group By Summary: [Black bar with arrow]
 Progress: [Red bar] Summary: [Black bar with arrow] Rolled Up Milestone: [White diamond] Split: [Dotted line] Project Summary: [Grey bar with arrow]

WATERS (DOMESTIC WELLS)

ID	Task Name	Qtr 1, 2005	Qtr 2, 2005	Qtr 3, 2005	Qtr 4, 2005	Qtr 1, 2006	Qtr 2, 2006	Qtr 3, 2006	Qtr 4, 2006	Qtr 1, 2007	Qtr 2, 2007	Qtr 3, 2007
161	Tucumcari DW											
162	Sort and Compare											
163	Abstract											
164	Images to Web											
165	QA and Archive											



Project: WATERS
Date: Thu 11/13/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			
